


# Construction Schedule - Townsite Area Utility Upgrades

Date: 2024-12-02

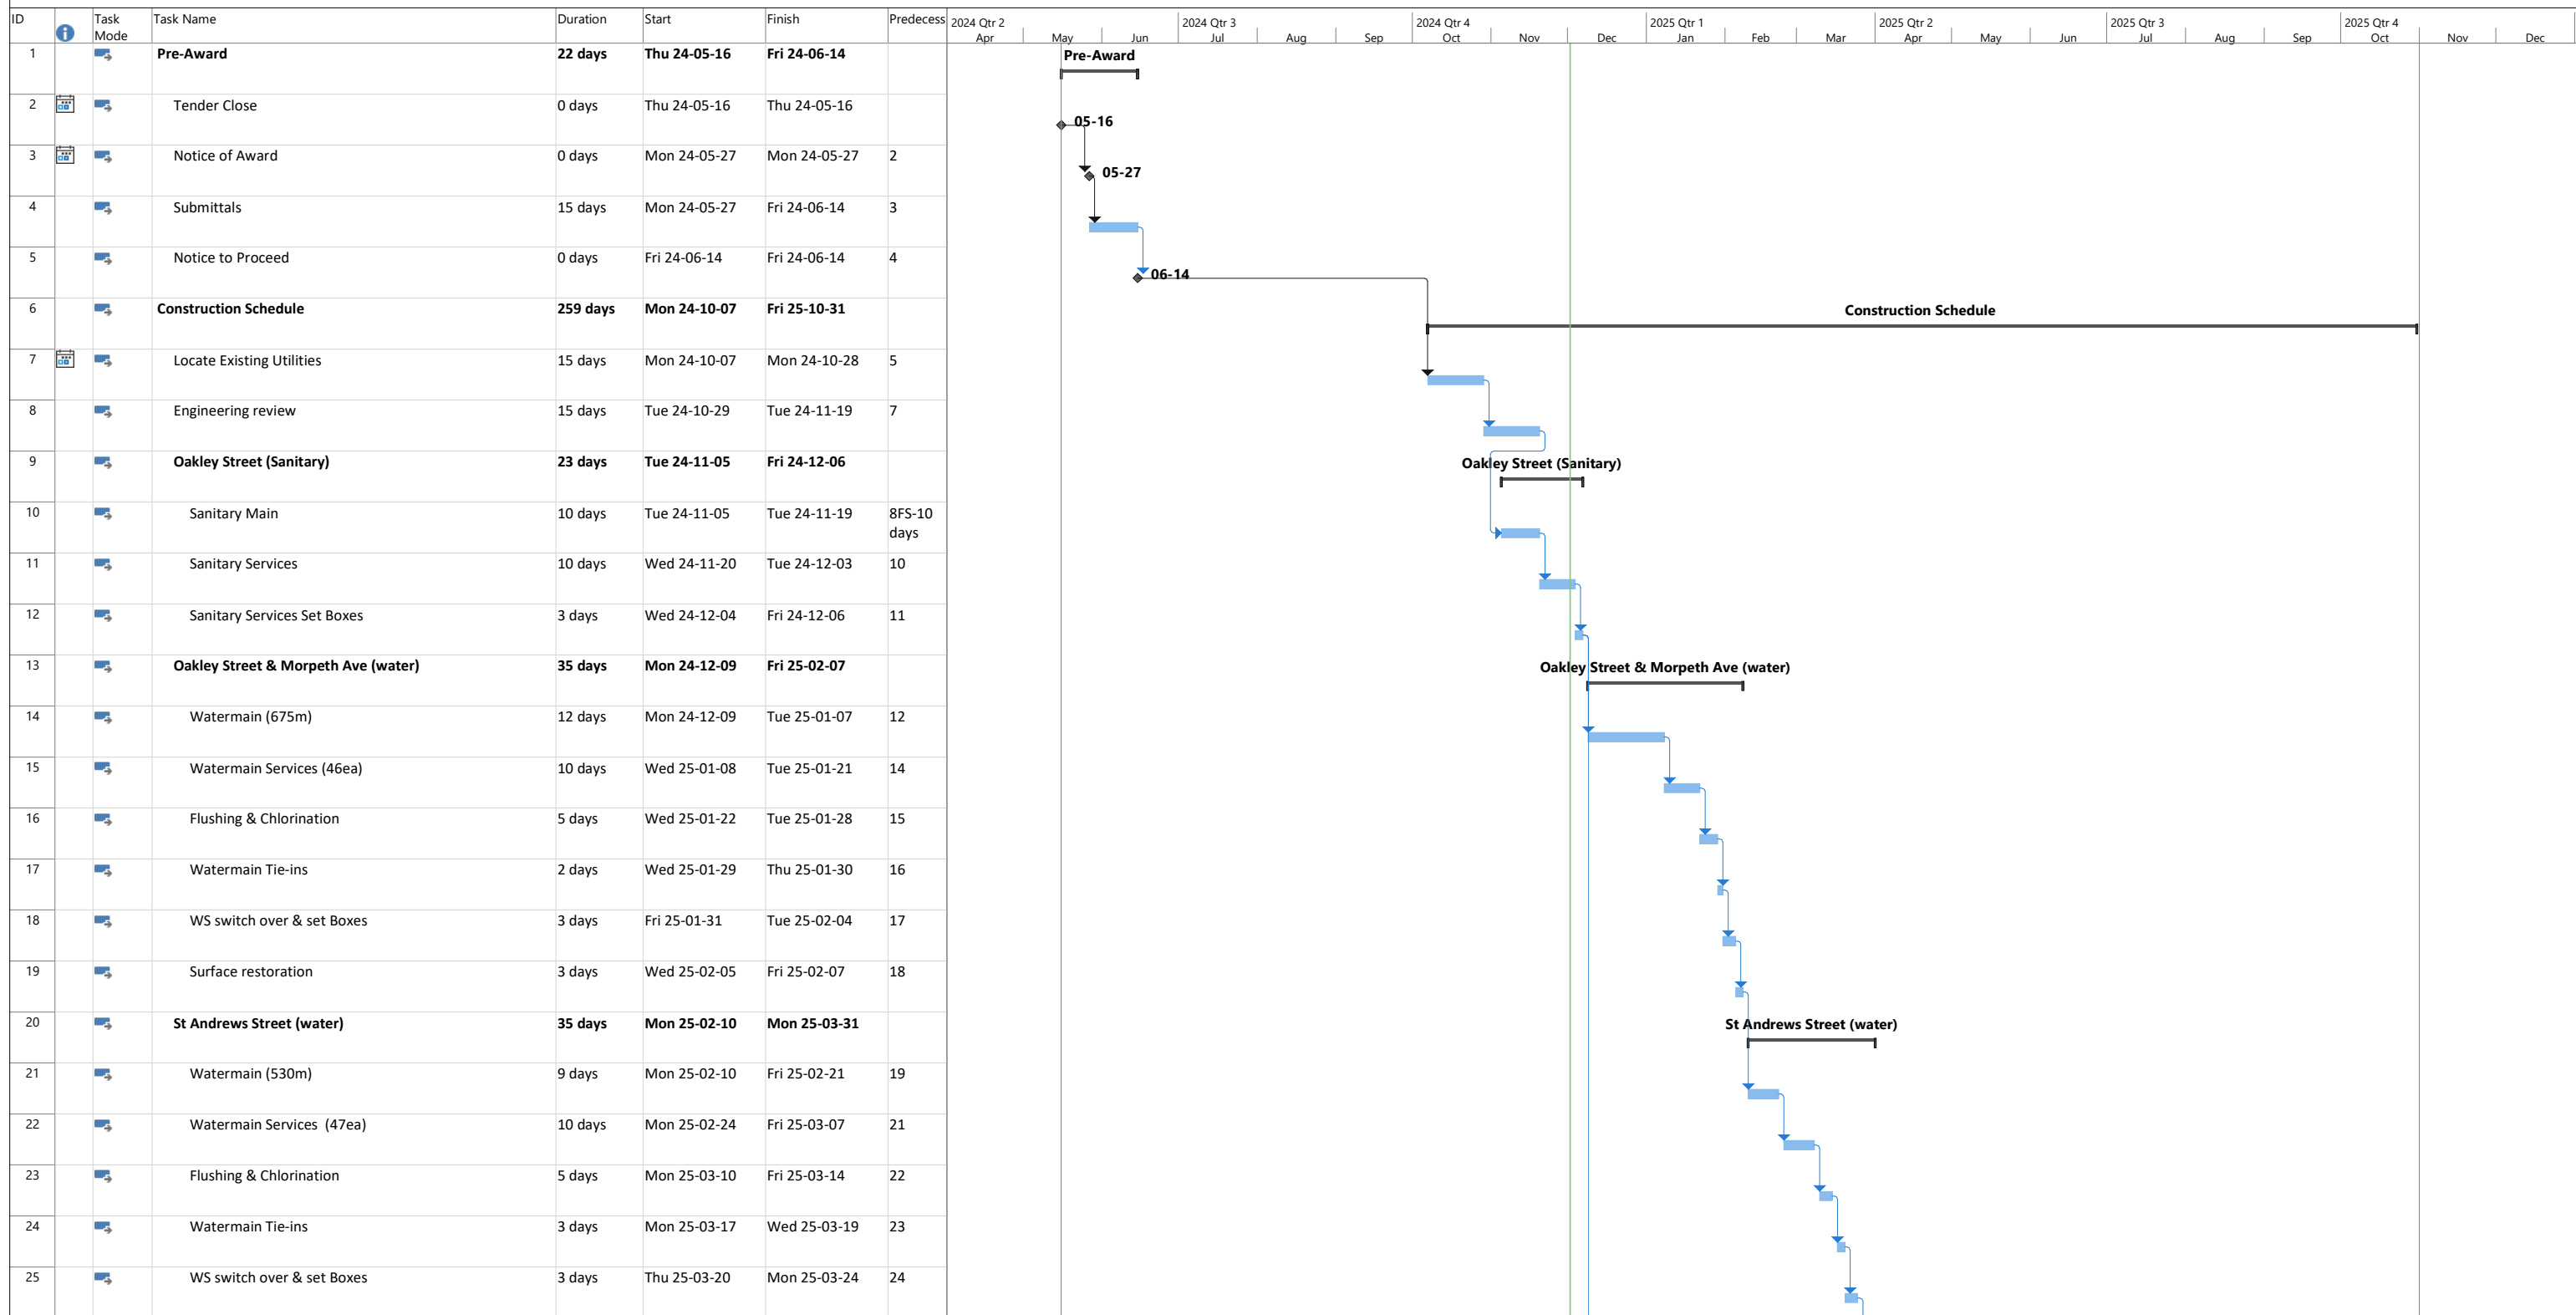

CIVIL CONTRACTORS | Breaking new ground.


Task		Summary		Inactive Milestone		Duration-only		Start-only		External Milestone		Manual Progress	
Split		Project Summary		Inactive Summary		Manual Summary Rollup		Finish-only		Deadline			
Milestone		Inactive Task		Manual Task		Manual Summary		External Tasks		Progress			

NOTE: This Construction Schedule was created at the time of project award and may be changed by Knappett Industries at any time due to unforeseen circumstances, weather and schedule changes.

# Construction Schedule - Townsite Area Utility Upgrades

Date: 2024-12-02

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessor	2024 Qtr 2			2024 Qtr 3			2024 Qtr 4			2025 Qtr 1			2025 Qtr 2			2025 Qtr 3			2025 Qtr 4		
							Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec
26		Surface restoration	5 days	Tue 25-03-25	Mon 25-03-31	25																					
27		<b>Oakley Roadworks</b>	11 days	Tue 25-04-01	Tue 25-04-15																						
28		Remove Asphalt	3 days	Tue 25-04-01	Thu 25-04-03	26																					
29		Place & compact Base Gravels	3 days	Fri 25-04-04	Tue 25-04-08	28																					
30		Fine grade Base Gravels	2 days	Wed 25-04-09	Thu 25-04-10	29																					
31		Paving	1 day	Fri 25-04-11	Fri 25-04-11	30																					
32		Line Painting	2 days	Mon 25-04-14	Tue 25-04-15	31																					
33		<b>Millstone Ave (Sanitary)</b>	25 days	Wed 25-04-16	Thu 25-05-22																						
34		Sanitary Main	15 days	Wed 25-04-16	Wed 25-05-07	32																					
35		Sanitary MH2 Tie-in	1 day	Thu 25-05-08	Thu 25-05-08	34																					
36		Sanitary Services	5 days	Fri 25-05-09	Thu 25-05-15	35																					
37		Sanitary Services Set Boxes	2 days	Fri 25-05-16	Tue 25-05-20	36																					
38		Surface restoration	2 days	Wed 25-05-21	Thu 25-05-22	37																					
39		<b>Millstone Ave (Water)</b>	55 days	Fri 25-05-23	Mon 25-08-11																						
40		Watermain (650m)	11 days	Fri 25-05-23	Fri 25-06-06	38																					
41		CATALYST SHUTDOWN	5 days	Wed 25-06-18	Tue 25-06-24	40,71																					
42		Watermain Services (63ea)	13 days	Wed 25-06-25	Mon 25-07-14	41																					
43		Flushing & Chlorination	5 days	Tue 25-07-15	Mon 25-07-21	42																					
44		Watermain Tie-ins	5 days	Tue 25-07-22	Mon 25-07-28	43																					
45		WS switch over & set Boxes	4 days	Tue 25-07-29	Fri 25-08-01	44																					
46		Surface restoration	5 days	Tue 25-08-05	Mon 25-08-11	45																					
47		<b>Millstone Roadworks</b>	22 days	Tue 25-08-12	Thu 25-09-11																						
48		Remove Asphalt	5 days	Tue 25-08-12	Mon 25-08-18	46																					
49		Place & compact Base Gravels	5 days	Tue 25-08-19	Mon 25-08-25	48																					
50		Fine grade Base Gravels	4 days	Tue 25-08-26	Fri 25-08-29	49																					

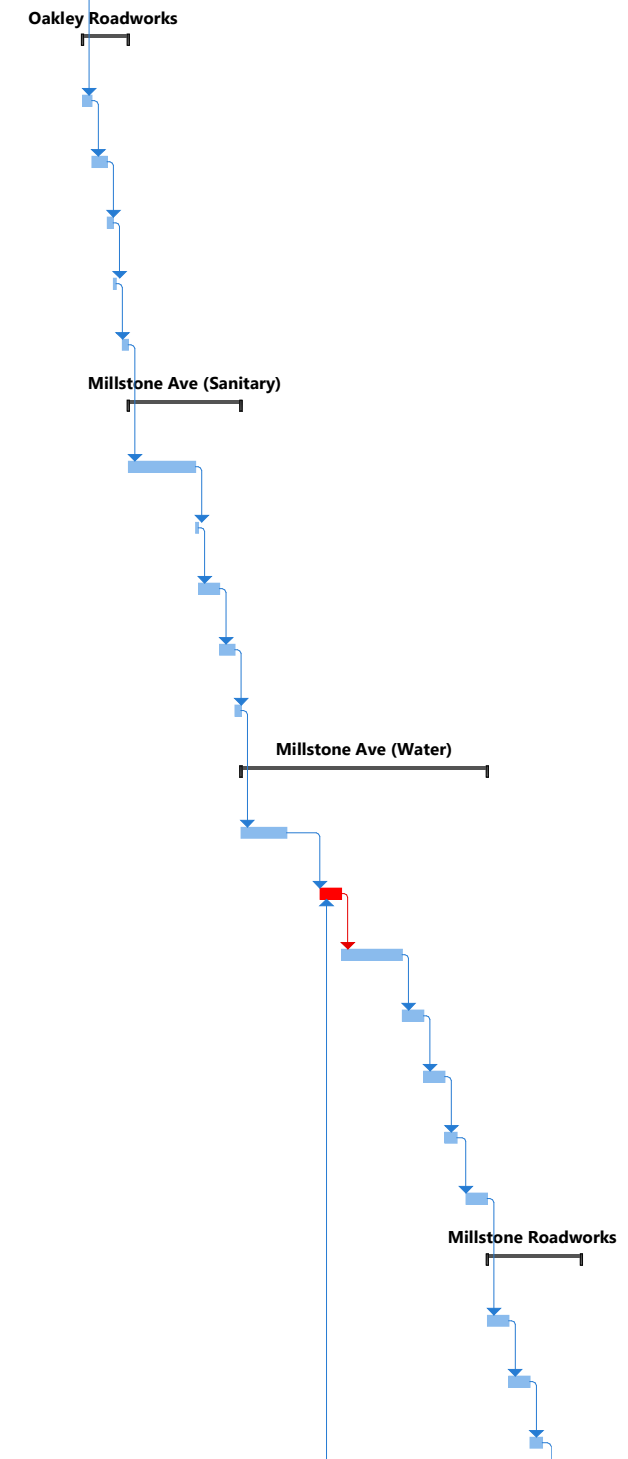

CIVIL CONTRACTORS | Breaking new ground.


Task		Summary		Project Summary		Inactive Task		Inactive Milestone		Manual Task		Inactive Summary		Manual Summary Rollup		Manual Summary		Start-only		Finish-only		External Tasks		External Milestone		Manual Progress		Progress	
Split																													
Milestone																													

NOTE: This Construction Schedule was created at the time of project award and may be changed by Knappett Industries at any time due to unforeseen circumstances, weather and schedule changes.

# Construction Schedule - Townsite Area Utility Upgrades

Date: 2024-12-02

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	2024 Qtr 2			2024 Qtr 3			2024 Qtr 4			2025 Qtr 1			2025 Qtr 2			2025 Qtr 3			2025 Qtr 4		
							Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec
51		Paving	3 days	Tue 25-09-02	Thu 25-09-04	50																					
52		Line Painting	5 days	Fri 25-09-05	Thu 25-09-11	51																					
53		<b>Chelsea Street to St. George Street (water-2nd Crew)</b>	<b>70 days</b>	<b>Mon 24-12-09</b>	<b>Mon 25-03-31</b>																						
54		Watermain (600m)	12 days	Mon 24-12-09	Tue 25-01-07	12																					
55		Watermain Services (52ea)	12 days	Wed 25-01-08	Thu 25-01-23	54																					
56		Flushing & Chlorination	5 days	Fri 25-01-24	Thu 25-01-30	55																					
57		Watermain Tie-ins	3 days	Fri 25-01-31	Tue 25-02-04	56																					
58		WS switch over & set Boxes	3 days	Wed 25-02-05	Fri 25-02-07	57																					
59		Storm Works	5 days	Mon 25-02-10	Fri 25-02-14	58																					
60		<b>HARMAC SHUTDOWN</b>	<b>30 days</b>	<b>Tue 25-02-18</b>	<b>Mon 25-03-31</b>	<b>59</b>																					
61		<b>Cadogan Street &amp; Northumberland Ave (Water-2nd Crew)</b>	<b>42 days</b>	<b>Tue 25-04-01</b>	<b>Fri 25-05-30</b>																						
62		Watermain (780m)	13 days	Tue 25-04-01	Thu 25-04-17	60																					
63		Watermain Services (65ea)	13 days	Mon 25-04-21	Wed 25-05-07	62																					
64		Flushing & Chlorination	5 days	Thu 25-05-08	Wed 25-05-14	63																					
65		Watermain Tie-ins	3 days	Thu 25-05-15	Tue 25-05-20	64																					
66		WS switch over & set Boxes	3 days	Wed 25-05-21	Fri 25-05-23	65																					
67		Surface restoration	5 days	Mon 25-05-26	Fri 25-05-30	66																					
68		<b>Gilvin Ave (Water-2nd crew)</b>	<b>18 days</b>	<b>Mon 25-06-02</b>	<b>Wed 25-06-25</b>																						
69		Watermain (300m)	4 days	Mon 25-06-02	Thu 25-06-05	67																					
70		Watermain Services (13ea)	3 days	Fri 25-06-06	Tue 25-06-10	69																					
71		Flushing & Chlorination	5 days	Wed 25-06-11	Tue 25-06-17	70																					
72		Watermain Tie-ins	3 days	Wed 25-06-18	Fri 25-06-20	71																					
73		WS switch over & set Boxes	1 day	Mon 25-06-23	Mon 25-06-23	72																					
74		Surface restoration	2 days	Tue 25-06-24	Wed 25-06-25	73																					
75		Substantial Completion	0 days	Fri 25-10-31	Fri 25-10-31	74,52																					

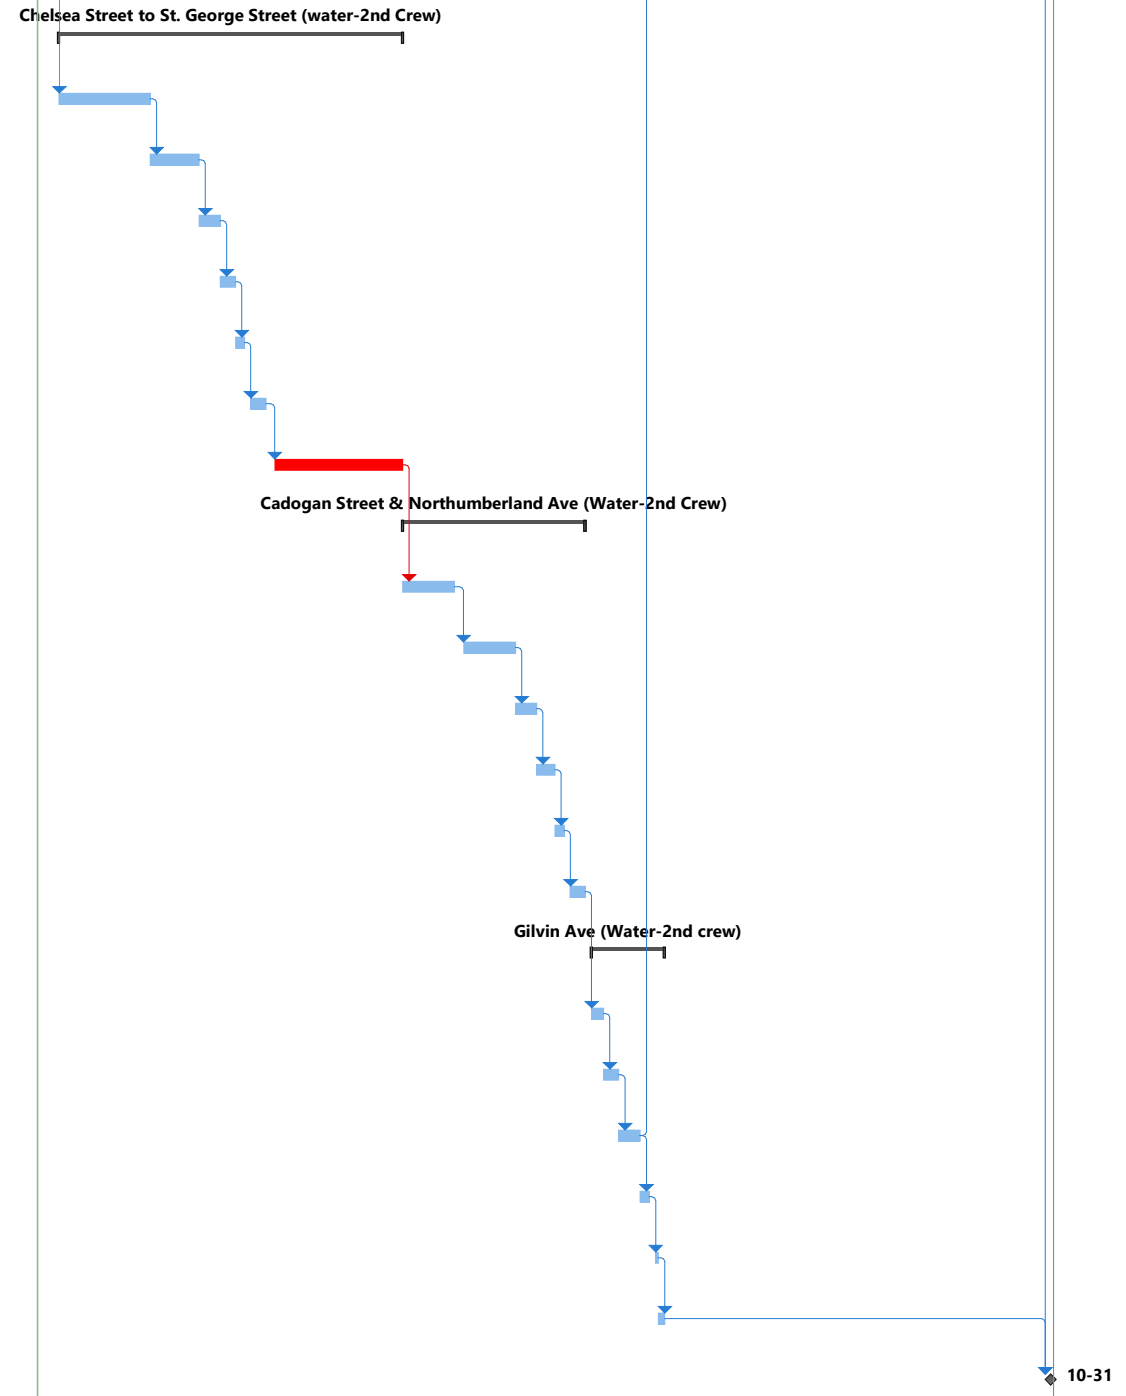

Task		Summary		Inactive Milestone		Duration-only		Start-only		External Milestone		Manual Progress	
Split		Project Summary		Inactive Summary		Manual Summary Rollup		Finish-only		Deadline			
Milestone		Inactive Task		Manual Task		Manual Summary		External Tasks		Progress			

NOTE: This Construction Schedule was created at the time of project award and may be changed by Knappett Industries at any time due to unforeseen circumstances, weather and schedule changes.
